## The South Fork Trail

#### **Segment 1: Bishop Creek**

Report Date: July 15, 2022.

Trail Stats -- Mileage: 3.1 miles; Elevation Gain/Loss: 1,073 feet. 4,938' (top), 3,865' (bottom);

Estimated Duration: Going down (2 hours). Going up (3 hours)

**Status:** <a href="https://www.google.com/maps/d/viewer?mid=1cK-eXqe6|X6YY26">https://www.google.com/maps/d/viewer?mid=1cK-eXqe6|X6YY26</a> JrNhdLB370vl92aL&ll=37.60174944115586%2C-119.79676961792443&z=12

**Overall Goal** -- To repair and maintain trail for non-motorized users (hikers, runners, backpacking and equestrians). Dogs and mountain bikes are not allowed in the section of trail located in Yosemite National Park. As the east entry to the South Fork Trail, this is a high priority trail.





**Project History** – The initial assessment of this trail by Mariposa Trails occurred on February 18, 2018. At that time, dense stands of Mountain Mahogany clogged the trail many of the Ponderosa Pine trees were still standing; although many were dead due to the bark-beetle infestation. In August 2018, a backfire to stop the Ferguson Fire, burned through the area. In 2020, the Mountain Mahogany was removed, as well as many of the fallen trees. In 2021, a CCC crew widened the trail, shifted a small section of trail out of a Willard Creek riparian zone, and made it easier for stock to enter Bishop Camp.



Past Activities -
Except where noted, all categories are described as "number of."

YEAR	OUTINGS	VOL-HOURS	TREES	TREAD	ROCKWORK	BRUSH	CAMPSITE
			CLEARED	REPAIR (ft)		REMOVED	IMPROVE
2018	1	18	0	4,000	0	25	0
2019	2	67	11	800	0	25	0
2020	5	95	9	500	0	300	0
2021	1+CCC	16	32	7,000	0	44	1
2022							






### **PROPOSED WORK: "South Fork Merced River Trails Project"**

#### TASK # Work by Mariposa Trails Volunteers

- 1. Install U.S. Forest Service Boundary Sign and trailhead wayfinding & informational sign boards
- 2. Buck 10 fallen trees from trail
- 3. Remove brush and saplings encroaching onto trail by: (1) extract buck-brush, deer-brush & mountain mahogany by roots (20 hrs labor); and, (2) clipping back brush (8 hrs labor)
- 4. Clear dead ladder fuel from trunks of oak trees in the trail corridor.
- 5. Remove 10 fallen trees at "Camp Bishop."
- 6. Install a directional/mileage/place-name sign(s)

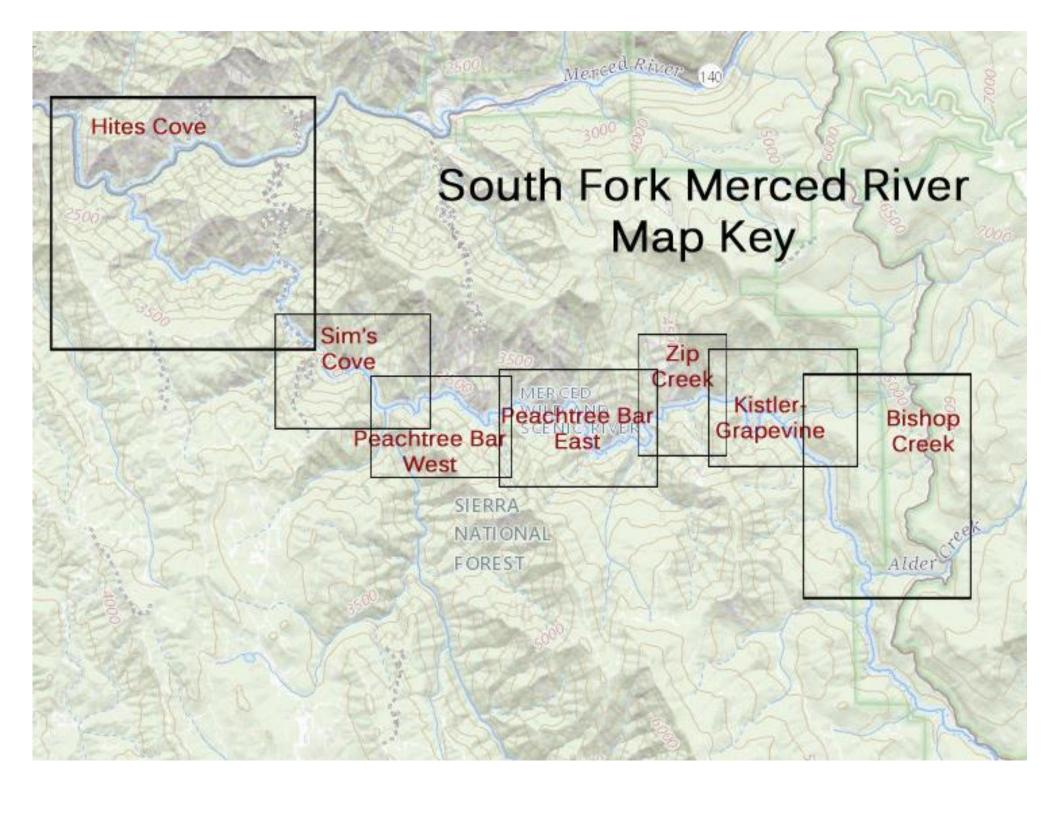

# **SOUTH FORK TRAIL-** SEGMENT 1: Bishop Creek

